

MENTORN HER STATE OF THE STATE

# DTIC FILE COPY



INTEGRATED FACILITIES
MANAGEMENT PLAN

April 1984

Douglas K. Ault John H. Cable William A. Woodring

Prepared pursuant to Department of Defense Contract No. F33657-83-C-0444 (Task AS301). Views or conclusions contained in this document should not be interpreted as representing official opinion or policy of the Department of Defense. Except for use for Government purposes, permission to quote from or reproduce portions of this document must be obtained from the Logistics Management Institute.

This document has been approved for public release and sale, its document is unlimited.

LOGISTICS MANAGEMENT INSTITUTE 4701 Sangamore Road P.O. Box 9489 Washington, D.C. 20016 APR 2 3 1987

4 28 109

#### ACKNOWLEDGMENT

In the preparation of this Facilities Management Plan, LMI required a great amount of data on organizations and facilities and extensive information on missions and requirements. The data and information have been willingly provided by personnel throughout the Aeronautical Systems Division (ASD) of the Air Force Systems Command (AFSC). LMI sincerely appreciates the cooperation of all ASD staff personnel involved in supporting this effort.

The data gathering effort by the Civil Engineering Directorate at ASD (ASD/DE) is especially appreciated. This massive effort required the accumulation of data from five different sources and building-by-building updating of records and drawings. The finished product not only provided LMI with a data base for this study but also provided ASD for the first time with a consolidated data base that can be expanded and improved for future facilities planning. All those involved can take pride in that accomplishment. LMI wishes to offer special thanks to Mr. Thomas J. Ridel who coordinated the data effort both within ASD/DE and with the other organizations involved. We also wish to thank Lt. Col. R. V. Christiansen, USAF, Director of Programs Division, Civil Engineering Directorate, for his interest, support, and guidance throughout the project.



## Executive Summary

#### INTEGRATED FACILITIES MANAGEMENT PLAN

The Aeronautical Systems Division (ASD) of the Air Force Systems Command provides technological support for and management of aeronautical weapons systems development, including research, development, systems engineering, and evaluation. The growing complexity of aircraft systems and the rapid rate of change in technology have resulted in expanding missions for ASD, especially in the area of systems integration. This trend is expected to continue well into the 1990s as ASD enters the era of automated aircraft.

To support its mission, ASD houses almost 10,000 employees in some 160 facilities throughout Area "B," Wright-Patterson Air Force Base, Ohio. Many of these facilities are old and in marginal-to-poor condition. Most were not designed for modern technical work and are unsuitable to support today's ASD mission. The facilities are small and scattered, and have splintered the organization. As a result, interaction and technology transfer have been severely limited. The total space available to ASD is barely adequate to accommodate today's needs, and the deficiency will become worse as ASD's mission continues to grow.

To overcome these problems, we have developed an integrated Facilities Management Plan whose major goals are:

- To provide modern facilities that satisfy the functional support requirements of the technical mission;
- To improve communication and the transfer of technology to support systems engineering and integration; and
- To provide the flexibility needed for growth and change of the ASD mission.

In order to meet those goals, we recommend the following basic strategies:

- Maximize the utilization of existing facilities;
- Consolidate functional organizations within zones;
- Systematically replace aging and unsuitable facilities and dispose of facilities no longer needed.

To support those strategies, some military construction will be required. We evaluated and modified existing construction proposals and recommend three major projects:

- A 68,000 square foot, \$9.7 million addition to Building 485 for the Deputy for Engineering, including an 8,000 square foot alteration;
- A 133,500 square foot, \$16.5 million addition to Building 620 for the Avionics Laboratory;
- A 400,000 square foot, \$60 million Systems Management Engineering Facility to be constructed in two or three phases.

Those construction projects should be complemented by relocations, modifications, and demolitions that support the planning strategies.

THE CONTRACT CONTRACT BEAUTIFUL SPECIAL PROPERTY SERVICES SERVICES SERVICES SERVICES SERVICES SERVICES SERVICES

The Facilities Management Plan is not a static document; rather, it is a starting point -- a baseline from which detailed and continued planning should proceed. ASD must now organize its facility planning staff to ensure that it develops the internal capability to implement the Plan. ASD must also conduct follow-through planning for short-term and long-term needs and must coordinate all aspects of the Facilities Management Plan with the host command and tenant commands.

# TABLE OF CONTENTS

		Page
	PREFACE	ii
	EXECUTIVE SUMMARY	iii
Š	LIST OF FIGURES	vi
	LIST OF TABLES	vi
<b>X</b>	1. INTRODUCTION	1- 1
Š	2. EXISTING CONDITIONS AND FACILITY REQUIREMENTS	2- 1
	Adequate Space	2- 1 2- 5 2- 6 2- 7 2- 8
	Long-Term Goals and Planning Strategies	3- 2 3- 5 3- 6 3- 7 3- 8
8	4. IMPLEMENTATION	4- 1
	Organization	4- 1 4- 2 4- 3
	APPENDIX B: EVALUATION OF EXISTING CONSTRUCTION ALTERNATIVES	
	APPENDIX C: GLOSSARY OF TERMS	

# LIST OF FIGURES

FIGURE		Page
1-1	Functional Organization of Aeronautical Systems Division	1- 2
3-1	Area "B" Site Plan - Zone Concept	3- 4
	LIST OF TABLES	
TABLE		Page
2-1	ASD Floor Area Distribution	2- 2
2-2	Air Force Standards for Office and Administrative Support Space	2- 3
2-3	ASD Area "B" Building Efficiency Ratios	2- 3
2-4	Office and Administrative Support Space Requirements	2- 4
2-5	Air Force Condition Code Definitions	2- 6
3-1	Relocation Actions Associated with Facilities Management Plan MCPs	3- 7
3-2	Other Possible Relocations in Support of Facilities Management Plan	3- 8
3-3	Area "B" Buildings Recommended for Demolition	3- 9


#### 1. INTRODUCTION

The mission of the Aeronautical Systems Division (ASD) of the Air Force Systems Command (AFSC) is to provide technological support for the development of aircraft weapons systems, including research, development, systems engineering, and evaluation. These ASD functions are carried out by the seven organizational groupings shown in Figure 1-1. The Headquarters group, of course, provides management and control of the overall program and with the help of the Organizational Support group, performs all the normal command type functions and services. The Acquisition Management or Systems Program Office (SPO) group is directly involved in the development and procurement of aeronautical systems and is directly supported by the Specialized Management and Functional Management groups. In the latter group, the Deputy for Engineering (EN) has specific responsibilities in the area of systems engineering and integration. The Air Force Wright Aeronautical Laboratories (AFWAL) and the four component laboratories have the major responsibility for research and development (R&D) and are involved also in evaluating potential usefulness of new technologies. AFWAL has only recently (1983) been placed under ASD, and this major organizational change has affected both program and support requirements.

さいことがない 人のかんかん 大きにはなっている 人のおおおけれる からなからない こうじょうしょ 国のシングラン こうじゅんしん はず

Six ASD organizational groups are located in Area "B" of Wright-Patterson Air Force Base; most of the 4950th Test Wing is located elsewhere. Wright-Patterson is an Air Force Logistics Command (AFLC) installation, which makes ASD a tenant even though it occupies a majority of the space within Area "B." Other major tenants in Area "B" include the Air Force Institute of Technology (AFIT), the Air Force Museum, the Aerospace Medical Division, and several AFLC organizations.

FIGURE 1-1. FUNCTIONAL ORGANIZATION OF AERONAUTICAL SYSTEMS DIVISION

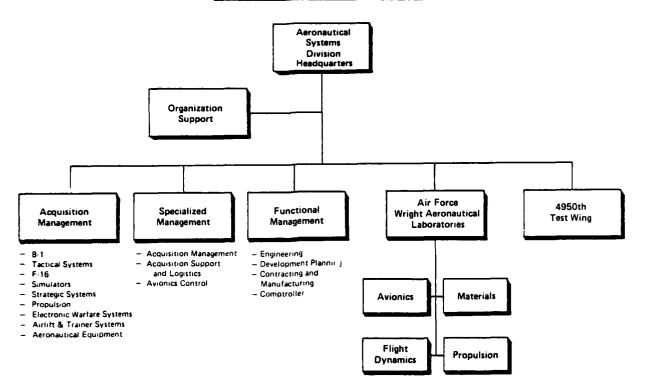

Area "B," the former Wright Field, is a 2,401 acre area containing more than 200 major buildings. Although the organizations and names have changed throughout the years, Area "B" has always been the home of aircraft weapons systems development. Construction of this part of the base began in the 1920s, and some of the original facilities are still in use today. Most buildings were built during World War II, giving ASD facilities an average age of 38 years. The buildings for systems management are even older, averaging 53 years. Aircraft and weapons systems technology have changed drastically in that time as have the R&D techniques used for developing modern aircraft systems, and the changes continue today at an ever-increasing pace. Because of the dynamic nature of aircraft R&D, many organizations are housed in facilities that do not adequately support their current technical needs. The

growing complexity of aircraft systems and the resulting expansion in ASD's systems engineering and integration mission will place an even greater burden on these outmoded facilities in the years to come.

These problems have been recognized by various ASD organizations, and they have attempted to correct the deficiencies through facility modernization and new construction. However, many of the improvements have been only cosmetic, and the construction projects have addressed only a portion of the needs of individual organizations rather than the overall needs of ASD. This situation has resulted in the piecemeal development of competing projects that are difficult to justify individually.

An integrated facility management plan is needed to provide a framework for sound, coordinated decisions as the basis for improving the overall condition of ASD facilities. Such a plan will support systematic facilities planning and encourage the best possible utilization of all current and projected facilities.

This report discusses the current ASD facilities and their problems (Chapter 2). A tabulation of the facilities and organizations for which these problems exist is given in Appendix A. It then presents a specific Facilities Management Plan to meet ASD facility requirements through 1991 (Chapter 3). This Plan is a hybrid of five proposed alternatives that are briefly stated in Chapter 3 and are discussed in more detail in Appendix B along with the evaluation methodology used to develop the Plan. The implementation of the Plan is discussed in Chapter 4.

## 2. EXISTING CONDITIONS AND FACILITY REQUIREMENTS

In evaluating existing conditions and assessing ASD facility requirements, we considered the following major criteria:

- Adequate Space: square footage required to house the function;
- Condition: building integrity;
- Suitability: appropriateness for the mission; and
- Proximity: closeness to other buildings/functions, ease of travel/interaction, and ease of technology transfer.

The existing conditions at ASD, insofar as each of these characteristics is concerned, may be summarized as follows:

- Adequate Space: some overcrowding and deficiency exist and will increase as ASD's mission grows;
- Condition: overall, facilities are marginal and becoming worse with age;
- Suitability: many facilities are not adequate for the current mission; and
- Proximity: segments of many key organizations are scattered, limiting interaction and technology transfer.

The combination of these problems presents a picture of less-than-adequate facilities that are already adversely affecting ASD mission capabilities. The situation will worsen as facilities age, missions expand, and technology changes. More details on the current state of each characteristic are presented in the following sections.

## ADEQUATE SPACE

THE SECOND STREET OF THE PROPERTY OF THE PROPERTY INTERCEDIAL WASHINGTON OF THE PROPERTY OF TH

ASD currently occupies approximately three million net square feet in Area "B." That space is distributed by type as shown in Table 2-1. ASD's space problems fall in two general categories: (1) office/administration and (2) special purpose, which includes R&D, storage, shop, and other. Office and

administrative support space is discussed first since the requirements are based on number of personnel and are generally more straightforward.

TABLE 2-1. ASD FLOOR AREA DISTRIBUTION

TYPE	AREA (SQ. FT.)	PERCENTAGE OF TOTAL
Office	1,060,595 <sup>a</sup>	36.2
Admin. Support	98,085	3.3
Special Purpose	326,303	11.1
R&D	1,033,426	35.3
Shop	205,106	7.0
Storage	125,004	4.3
Other	82,516	2.8
TOTAL	2,931,035	100

aSince 460,841 square feet (43%) of this is SPO area, only 599,754 square feet (20.5%) is actually classified as office space.

Standards for office space and administrative support space are set forth in Air Force Manual 86-2, and depicted in Table 2-2. As shown, the total for office space and administrative support space must lie within the range of 115 to 130 square feet per person. The lower number is applied for newer buildings with net-to-gross efficiency ratings in the neighborhood of 80 percent. The ASD buildings in Area "B" are old and were designed in an era when efficiency rates were much lower. Additionally, many of the buildings currently in use as offices were originally designed for other purposes, which also lowers the efficiency rates. The overall average efficiency rate for ASD buildings in Area "B" is about 72 percent, the average for systems management spaces is even lower. If the net floor area efficiency is the same as total building efficiency, the ASD requirements for net floor area are well above 130 square feet per person as shown in Table 2-3. Using the maximum allowable

TABLE 2-2. AIR FORCE STANDARDS FOR OFFICE AND ADMINISTRATIVE SUPPORT SPACE

	MINIMUM (SQ.FT.)	MAXIMUM (SQ.FT.)
Net Floor Area P.B.O.	115	130
Net Office Area P.B.O.	80	90
Administrative Support for 80 sq. ft. office	35	50
Administrative Support for 90 sq. ft. office	25	40

ap.B.O. - Per building occupant.

SOURCE: "Civil Engineering Programming, Standard Facility Requirements," Air Force Manual 86-2, Department of the Air Force, 1 March 1973.

TABLE 2-3. ASD AREA "B" BUILDING EFFICIENCY RATIOS

大きな意見さいことでは18mのでいっては18mのではない。18mのではないないなどは1mmではないないでは、1mmのではないなど、美元のでは19mのではないないない。18mのではないないない。18mのでは18mので

	BUILDING EFFICIENCY <sup>a</sup>	NET FLOOR AREA (SQ.FT. P.B.O.)
Air Force Standard	0.80 to 0.85	115 to 130
ASD Average	0.72	128 to 153 (140 avg.)

<sup>&</sup>lt;sup>a</sup>Net floor area/gross floor area.

figure of 130 square feet per person and current total personnel numbers, <sup>1</sup> the ASD requirement for office and administrative space, as shown in Table 2+4, is 1.28 million square feet. A comparison of this requirement with the current

<sup>&</sup>lt;sup>b</sup>Net Floor Area - Net Office Area = Administrative Support Space.

Personnel figures include ASD straight-line and other government personnel such as TAC, MAC, SAC, LOG Command, Army, Foreign Liaison, etc.

ASD figure for office and administrative space from Table 2-1 shows a shortage of about 120,000 square feet. ASD is rapidly moving into the era of office automation, and the time is coming when a large percentage of ASD personnel will have terminals at the individual work stations, which will serve to increase office square footage requirements even more.

TABLE 2-4. OFFICE AND ADMINISTRATIVE SUPPORT SPACE REQUIREMENTS

AREA	SQUARE FEET
Current Space:	
ASD Total Office and Admin. Support	2,930,806 1,158,670
Required Space: <sup>a</sup>	
8544 ASD Personnel 874 Above-Line Personnel <sup>b</sup> 9818 ASD Total	1,162,720 113,620 1,276,340
Deficiency	117,670

<sup>&</sup>lt;sup>a</sup>Based on 130 square feet per person Air Force standard.

Thus far, only office and administrative requirements have been discussed. Special-purpose space is provided on an as-needed basis and it is often assumed to be adequate. However, significant and numerous shortages in special-purpose space were also noted in evaluations of the various organizations. Appendix A, Section I, tabulates the specific facilities by organization that have space problems.

Conference room space is another area of serious concern. Under the standards, conference room space is included under the administrative support category. However, ASD's unique teamwork approach in support of its systems

bIncludes AFAL, TAC, SAC, other government personnel, cooperatives, and contractor personnel (estimated at 15 percent).

engineering and integration mission makes extra conference room space a necessity. The security aspects of ASD's work imposes a need for classified conference rooms, which places this requirement in the special-purpose category. CONDITION

The condition of ASD buildings, as reported by the Base Civil Engineer, is based on a three-level condition code outlined in Table 2-5. The Real Property Inventory Report compiled in September 1983 shows less than three percent of the ASD Area "B" inventory as Condition Code 3 (forced use). From that report, it appears that the condition of ASD assets is generally good. However, the Base Civil Engineer makes the condition assessment primarily on the adequacy of the building structure. Interior condition and adequacy of electrical, heating, cooling, ventilation systems, and energy efficiency do not appear to have a major impact. However, the environment within a building, especially the condition of electromechanical systems, is of great concern to ASD because of the technical nature of the R&D mission. Some significant problems in specific ASD facilities are shown in Appendix A, Section II.

The Real Property Inventory Report shows that most ASD facilities are in Condition Code 2, indicating some work is required to bring the buildings up to Code 1. In some cases, the work required is substantial. Through the FOCUS program, ASD has developed projects to upgrade various facilities at a total cost of more than \$75 million. Most of that money is to be invested in 40-year-old buildings that are approaching the limits of their useful life. The proposed projects may extend the life of those buildings for some limited time, but they cannot remove the need for eventual replacement. As is the case at most bases, Wright-Patterson Air Force Base has a large block of buildings built during the 1940s; in order to avoid block replacement in the

## TABLE 2-5. AIR FORCE CONDITION CODE DEFINITIONS

The Air Force real property condition codes define the physical condition and structural adequacy of facilities for meeting current mission requirements. The condition codes are:

Code 1: Usable -- Class A
Generally meets criteria and can house the mission with reasonable maintenance and without major alteration or reconstruction.

Code 2: Usable -- Class B
Upgrading is required and is practical. Although structurally sound, upgrading is required to be classified Code 1.

Code 3: Force Use
Cannot practically be raised to meet Code 1 standards but,
by necessity, must be continued in use for a short
duration until a suitable facility can be obtained.
Facility cannot be justifiably or economically improved or
upgraded.

<sup>a</sup>Three other codes; 4, 5, and 6, exist but are not applicable to this project.

1990s, ASD must begin now to plan for the systematic replacement of aging, marginal structures. This, then, is the ASD situation with regard to facilities condition: (1) specific problems in certain facilities, as shown in Appendix A, must be remedied immediately; (2) the overall condition is probably worse than the Base Civil Engineer's report indicates; and (3) the facility condition problem will become increasingly critical throughout the 1990s, requiring systematic replacement of a significant percentage of ASD facilities.

#### SUITABILITY

STATE PROTESTS, CALCULAR STATESTATE STATESTATE A CONTROL OF STATESTATE A CONTROL OF STATESTATE STATESTATE AND INCOME.

The condition of a building addresses only its physical characteristics.

A building can be in good condition and still be inadequate for a particular mission. For example, many ASD facilities were originally designed as hangars

and warehouses, and although the building condition may be good, it is not an adequate facility for sophisticated technical work. In many buildings, the layout, environmental systems, flexibility, and other specialized requirements are not adequate to support today's ASD mission. Even some of the facilities that were originally designed for laboratory or R&D uses are inadequate because of the rapid change of technology in recent years. Procedures and functions are not the same as they were 20, 30, or 40 years ago.

では、これのでは、一般などのでは、一般などのでは、一般などのでは、一般などのでは、一般などのでは、一般などのでは、一般などのでは、一般などのでは、一般などのでは、一般などのでは、「我们のない」という。

This suitability issue is, by far, the most serious facility problem experienced by ASD today, and it is one that directly affects the mission capabilities of the organization. It is a problem more important than overcrowding or physical deterioration of facilities. Appendix A, Section III, tabulates the facilities in which suitability problems are experienced by the various ASD organizations. Unsuitability was mentioned twice as often as any other problem by ASD managers in a survey of facilities concerns. It is a problem that cannot be corrected by short-term modifications or rehabilitations; it will require new construction. Improvements in this area can be expected to result in increased productivity of workers, better and faster transfer of technology, and improved morale and retention of skilled employees. Those benefits will yield real dollar payoffs in terms of better weapons systems delivered faster and at lower costs.

#### PROXIMITY

The final category considered in establishing facility requirements is proximity. Several ASD organizations, including the Deputy for Engineering, the Avionics Laboratory, and the Flight Dynamics Laboratory are operating in fractionated and scattered facilities throughout Area "B." The splintering of these organizations severely restricts interaction and the transfer of technology both within the individual organizations and throughout ASD as a

whole. The control and management of the technical programs is also effectively reduced because of this situation. Appendix A, Section IV, lists those facilities and organizations detrimentally affected by proximity problems.

The proximity problem cannot be accepted as a condition that must be tolerated since it has a real and growing impact on ASD's ability to perform its systems engineering and integration mission. As the Air Force enters the era of automated aircraft, that mission will become more and more important and integrated facilities to support the mission will also gain in importance. The ASD organizations must be brought together in centralized facilities that can house all those working on a specific technology. As in the case of problems with building conditions, this proximity problem requires new construction, and that construction must begin soon in order to support the ASD mission of the 1990s.

## CONCLUSION

ASD's current facilities problems require an integrated approach to improvements which must include:

- Additional and more efficient space;
- Systematic replacement of aging and deteriorating facilities;
- Provisions of modern technical facilities that meet basic functional requirements for today's technology;
- Consolidation of organizations in zones to allow better interaction within organizations and thereby stimulation of interaction between organizations;
- Flexibility to accommodate the growth and change that are inherent in the weapons systems acquisition process.

The plan described in the next chapter is based on a quantitative evaluation of five proposals to alleviate current facility problems (Appendix B). It provides a framework for long-term ASD facilities planning.

#### 3. ASD FACILITIES MANAGEMENT PLAN

We evaluated five proposed alternatives were evaluated to develop a facilities management plan that would provide solutions to the current ASD facilities problems through 1991. Four of the alternatives involved some degree of construction, and the fifth consisted of improvements to existing facilities with no new construction. This no-construction alternative was rejected as a stand-alone solution because it failed to overcome the problems cited in Chapter 2. The four construction alternatives were:

- Consolidation of EN functions in an enlarged building;
- An addition to the Avionics Laboratory;
- An addition to the Flight Dynamics Structures Test Facility;
- Construction of a Systems Management Engineering Test Facility (SMEF).

To evaluate these alternatives, LMI developed a method for quantifying the projected benefits of each. The alternatives were then compared to find the best combination of projects, and the results of the comparison were used to formulate the Facilities Management Plan presented in this chapter.

The ASD Facilities Management Plan is based on an evaluation of current and projected facility and mission requirements. It is not intended as a static prescription to solve all ASD facility problems, but rather, it should be viewed as a framework for future planning action. The details of the Plan may and should change, as requirements, missions, funding, manning, etc., change. However, the concepts upon which the plan is based and the direction suggested by it will serve ASD for the next decade or longer.

The Plan contains three elements: long-term goals, planning strategies, and specific actions. The specific actions recommended include new construction, relocations, and disposals. This chapter describes the long-term goals and planning strategies and details the construction, relocations, and disposals required to support the Plan. The alternatives and the methodology and analyses used in formulating the Plan are discussed in Appendix B. LONG-TERM GOALS AND PLANNING STRATEGIES

A study of ASD's mission requirements and current facilities situation suggests the following long-term goals:

- Provide modern facilities that meet functional requirements to support the technical mission;
- Improve interaction and the transfer of technology to support systems engineering and integration;
- Reduce facility-related costs that are draining R&D dollars;
- Provide the flexibility needed for growth and change of the ASD mission.

To meet these goals, basic strategies or approaches are needed. These strategies must be comprehensive enough to encompass the broad goals but specific enough to define a clear course of action. Additionally, the strategies must take into account existing constraints or obstacles. For example, new construction is often looked on as an ideal solution to facility problems. However, the real-world constraints of funding availability and dollar investment in existing facilities mean that construction must be limited. With these constraints and the previously defined goals in mind, we developed the following planning strategies for ASD:

- Maximize utilization of existing facilities;
- Consolidate organizations within zones to improve efficiency and strengthen research integration; and
- Systematically replace aging and unsuitable facilities and dispose of facilities no longer needed.

The first of these strategies is based on common sense, funding limitations, and recognition of the fact that existing facilities in Area "B" could support


the mission better through improved utilization, change of occupants, etc. For example, R&D space is currently being used for offices. This inefficient use of space does not properly support the mission and adds to total facilities costs.

The zone concept -- clustering major organizations together for better interaction -- was developed to support the goals of improving communications, integrating research, and facilitating technology transfer. Currently, ASD organizations are fragmented even at the lowest organizational level. The zone concept, as illustrated in Figure 3-1, is the first building block for improving technology transfer throughout ASD. This strategy also will improve flexibility by providing buffer or expansion zones for each organization. Currently, the only ways to accommodate change or growth at ASD are to "bump" another organization or accept overcrowded conditions. Either alternative degrades mission effectiveness. Constant moves and the required modifications add to facilities costs and are almost always funded from R&D dollars.

and andrews, provides provides proposed provides provides provides provided provides provides

The replacement of outmoded facilities will not only improve the ability of ASD to support the technical mission but should also improve communication and flexibility. New facilities are generally more efficient and need less maintenance, which will reduce facility costs. If the replacements are coupled with demolition of unusable facilities, the cost savings would be even greater, and the land made available through demolition will provide room for later expansions and reduce congestion. Replacement of facilities will also support the zone concept by allowing relocations.

These strategies then provide the basic guidelines along which the following plan was formed.

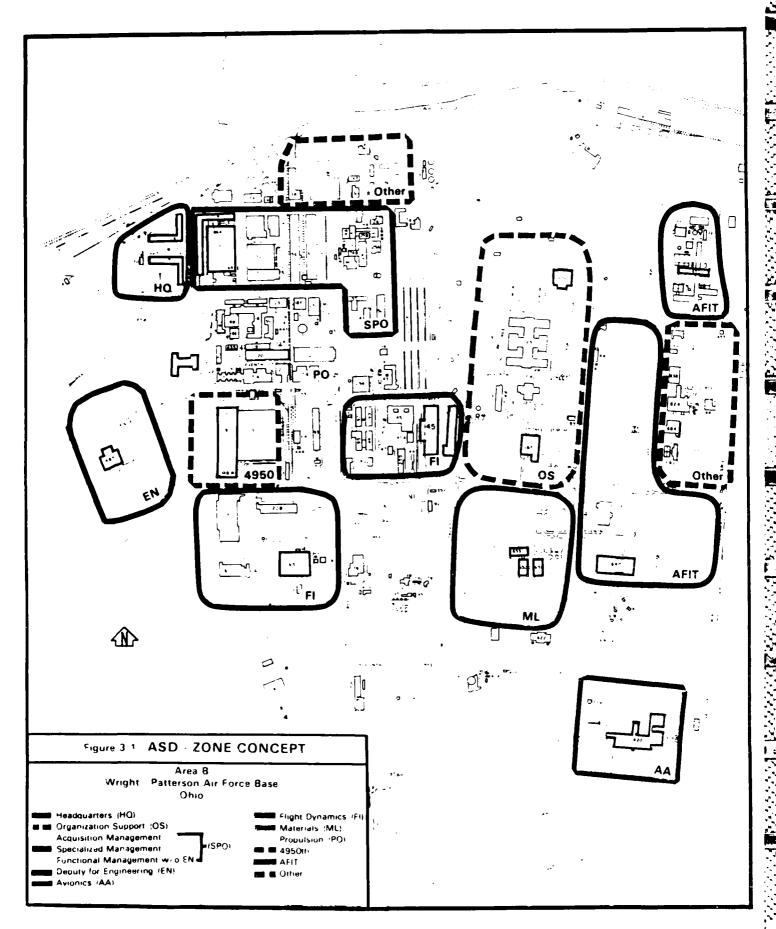

## NEW CONSTRUCTION

The recommended Plan requires three major construction projects in the FY87-FY90 timeframe. They are:

- An addition to Building 485 for EN functions;
- An addition to Building 620 for the Avionics Laboratory; and
- Construction of a new SMEF on current sites of Buildings 32, 51, and 56.

The first project will provide an area of approximately 68,000 square feet additional space and alteration of 8,000 square feet for the Deputy for Engineering, which will house five simulators for systems integration. This critical technical function will be removed from Building 156, a substandard, 40-year-old, temporary building. The additional space will also allow partial consolidation of EN functions. The estimated cost of the project in FY87 would be approximately \$9.7 million.

The \$16.5 million addition to Building 620 will provide about 134,000 square feet of additional space for the Avionics Laboratory to house a new consolidated electro-optics laboratory and new laboratory space for the electronic combat digital evaluation system. The additional office space provided as part of the project will release laboratory space in the existing building which is currently being used to house scientists and engineers. It will also allow consolidation of Avionics Laboratory program management and most of its personnel. A large amount of usable space will be vacated as a result of this move. Follow-on use for that space after the FY89-91 construction is discussed in the next section.

The third project recommended is construction of a SMEF. The exact size of this project has yet to be determined; it is, however, in the range of 300,000 to 400,000 square feet. The project could be completed in two phases in the FY89-FY90 period at a total cost of around \$60 million. The SMEF will

provide adequate and suitable space for all SPOs, thereby releasing space for supporting organizations. Substantial demolition also would accompany this project.

The follow-on aspects of the Facilities Management Plan -- relocations and demolition -- are discussed in the following sections.

## RELOCATIONS

Many ASD functional groups can be relocated as a result of the construction projects recommended in this Plan. The relocations should support the construction projects in following the basic strategies for ASD; specifically, they should adhere to the zone concept and ensure optimum utilization of existing facilities to support the mission. Table 3-1 lists the relocations associated with the Military Construction Projects (MCPs) proposed by this Plan. The EN and Flight Dynamics Laboratory (FI) relocations will both support the zone concept and result in more suitable facilities for those organizations. The relocations associated with the SMEF project are required because of the siting of that project. However, those relocations also support the zone concept and will provide better facilities for the organizations vacating the buildings recommended for demolition.

In addition to relocations resulting from the MCPs, other moves can be made in support of the overall plan. These moves, set forth in Table 3-2, are primarily for purposes of consolidation or better utilization of existing facilities.

Many of these proposed relocations, such as the FI moves out of the Building 24/25 complex, will open the way for demolition of unsuitable facilities.

TABLE 3-1. RELOCATION ACTIONS ASSOCIATED WITH FACILITIES MANAGEMENT PLAN MCP'S

В	UILDING	VACATE	OCCUPY
1.	ADDITION	TO BUILD	ING 485
	6 20 28A 156	EN EN EN	FI Pers.Ofc. Dispose Dispose
2.	ADDITION	TO BUILD	ING 620
	22 22B 24B 24C 450 622 Area C	AA <sup>a</sup> AA FI FI FI AA FI	FI FI bispose Dispose Dispose (Partial) Storage AFLC

BUI	LDING	VACATE	OCCUPY
3. <u>s</u>	MEF CO	NSTRUCTION	ı
	11	SMEF	EN
	16	SMEF	EN
	17	SMEF	Di <b>s</b> pose
	32	ML	Dispose
	39	SMEF	Dispose
	51	ML	Dispose
	56	SMEF/ML	Dispose
	57	SMEF/ML	Dispose
	91	SMEF	Dispose
	125	EN/	Tech.Lib.
	126	Source Selec. EN	AFIT, DISAM Pers.Ofc.
	167	Pers.Ofc.	Source Selec.
í	654	New Bldg.	ML
	655	New Bldg.	ML

<sup>&</sup>lt;sup>a</sup>AA: Avionics Laboratory; FI: Flight Dynamics Laboratory; DISAM: Defense Institute of Security Assistance Management; ML: Materials Laboratory.

#### DEMOLITION

Before considering the specific demolition actions recommended as part of the Plan, a brief discussion about how demolition fits into the overall plan is required. If new facilities are built on the justification that existing facilities are inadequate or unsuitable, it appears obvious that the old facilities should be torn down. Yet this seldom happens. The argument is often made, sometimes correctly, that an abandoned building can be used for other or temporary purposes. However, the impact of this line of reasoning over a period of years is that numerous inefficient, costly buildings are kept

Cleared area to be used to construct SMEF.

TABLE 3-2. OTHER POSSIBLE RELOCATIONS IN SUPPORT OF FACILITIES MANAGEMENT PLAN

BUILDING	ACTION
254	Rehabilitate for Gas Dynamics or other.
4A	Move 4950th personnel out.
821	Assign Avionics Laboratory personnel from Building 4A.
450	Assign to AFIT for "low observables".
22	Move Technical Library out.
125	Assign to Technical Library. Turn remainder of building over to AFIT or DISAM.
45	Move AFWAL out.
11	Install AFWAL.

on the books. In addition to the outright cost, keeping old buildings makes it very difficult to justify construction of modern facilities to support the mission. This situation exists in Area "B" at the present time. Old warehouses and hangars are being used to house technical functions simply because the space is there. The only way to overcome this problem is to include an aggressive demolition plan as part of the Facilities Management Plan.

Table 3-3 lists recommended demolitions for Area "B" through 1991. As indicated, many of these demolitions are tied to MCPs as a means for ensuring the resolve and funding necessary for the demolitions. Many other demolitions will require local funding, which should be programmed as part of the facilities budget.

## CONCLUSION

The Plan presented here is integrated in that it is based on total ASD requirements rather than on the needs of individual organizations; it is also integrated in that it includes construction, relocation, and demolition. The recommended actions are mutually supportive and significantly increase the benefits of the construction projects as shown in Appendix B. The details of

TABLE 3-3. AREA "B" BUILDINGS RECOMMENDED FOR DEMOLITION

CONSTRUCTION PROJECT	BUILDINGS TO BE DEMOLISHED
EN addition	28A,156
Avionics Laboratory Addition	24B,24C,450(P) <sup>b</sup> ,739
SMEF Construction	17,32,36,38,39, 51(P),56,57,91
Not related to Construction	29,30,42,50-A,55,59, 190,192,193,194,195, 196,197,198,434

<sup>&</sup>lt;sup>a</sup>Partial list; does not include minor structures, trailers, etc.

the Plan will change, but any changes must be based on an integrated systematic approach to facilities planning. This approach is possible only through a centralized facilities planning capability, which is discussed in more detail in Chapter 4.

 $<sup>^{</sup>b}(P)$ : Partial building demolition.

## 4. IMPLEMENTATION

The Facilities Management Plan outlined in Chapter 3 provides a framework for ASD facilities management planning through the 1990s. The three MCPs are the most visible aspect of the Plan, but they are only a part of it. Relocations, rehabilitation, and demolition also must fit into the Plan, and all these actions must be carefully coordinated and scheduled. For those reasons, implementation of the Plan is a major concern, no less important than its formulation. This chapter discusses three major aspects of the implementation: organization, coordination, and follow-through.

## ORGANIZATION

CODE TOURNESS CONTINUE SERVICES SERVICES SERVICES ALCOCATES SERVICES BOOKSERS AND ACCURATE ACCURATE CONTINUES OF CONTINUES

One of the most important steps in implementing the Facilities Management Plan is the establishment of a centralized facilities management capability. Currently, ASD facilities management is handled by 18 personnel working in six offices in different branches of the organization. Such a structure makes systematic planning and coordination almost impossible. There are two approaches to solving this problem:

- Develop a central facilities management office; and/or
- Maintain separate offices but coordinate actions through improved interaction.

Each approach has advantages and disadvantages. A central office would provide very tight control, but the decentralized approach might be more responsive to customer needs.

Probably the best solution is a combination of the two approaches, in which ASD organizations would maintain their own facilities staffs but be responsible to a common facilities resource manager. In order for this concept to work, all those involved must have a means for communicating data

on requirements, utilization, facility capacities, condition, etc., in a timely manner. This capability is not yet available at ASD; however, the data base compiled for this study provides a starting point. The next step should be some kind of simple microcomputer system for recording the data. Terminals should be available at all facilities offices to ensure access to data and provide a means for timely updating of information. The system does not have to be sophisticated, and no high-level software will be required. Any commercial data base management/spreadsheet package could be used. Of course, as personnel use the system and become more adept, many possibilities for enhancement would present themselves.

The processes of organizing and systematizing go hand-in-hand and will give ASD the internal capabilities needed for implementing the Facilities Management Plan. However, the ASD Plan cannot be implemented in isolation. The next section discusses the need for coordination with other organizations. COORDINATION

TO PARTIES. SOCIOOR PARTIES SERVICE SERVICES SER

■ ひとうじじとかる ■ でもらればなみない

It is extremely important that ASD as a tenant on an Air Force Logistics Command (AFLC) base coordinate any facility changes with the host. AFLC is responsible for all utilities, transportation, energy and environmental concerns, and facilities maintenance, as well as for the Base Comprehensive Plan (BCP). During this study, LMI contacted base personnel for general information on those items and briefed them on the general scope of this Plan ASD/DE has done some follow-up, but detailed coordination on construction projects and demolitions will be required for final implementation of the Plan. Close coordination between ASD and AFLC can only serve to strengthen the Plan as the planning process continues.

Douglas K. Ault, John H. Cable, and William V. Weedring. Building Inventory Data Base.

ASD must also coordinate its Plan with the other Area "B" tenants. AFIT, the Air Force Museum, 2750th, and the two AMD organizations all have MCPs scheduled for the FY85-89 period. ASD must become aware of how those projects will affect land use, utilities, and demolitions.

Finally, ASD must coordinate with the AFSC to ensure that the Facilities Management Plan developed for Area "B" is consistent with AFSC's long-term plans and command programs. As missions and emphases change, ASD will have to adapt its Plan to conform to the changing requirements. For that reason, the last step in implementation -- the follow-through -- is very important.

では、これのは、これのなどである。

## FOLLOW-THROUGH

The Facilities Management Plan will be of little use without appropriate follow-through. As stated earlier, the Plan outlined in this report is not a static one; rather, it is a starting point for future facilities planning. Requirements will change, details on siting, scope, etc., must be worked out, and follow-on projects must be developed. All of these actions will require a continuous planning effort. This report does not and cannot offer answers to all the questions and problems that will be encountered in the next five years since aircraft weapons systems development moves too fast for any document to cover all the concerns. The only answer is follow-through -- continued planning both short-term and long-term. Dr. Thomas Saaty states, "The object of planning is not to produce plans for others to use but to engage the users in their formulation and application. Effective planning cannot be done for individuals or organizations, it must be done by them." With this definition in mind, this project has provided an impetus: the planning process has been put in motion. The action can only be completed by effective follow-through.

Thr Thomas L. Saatv and Luis G. Vargas, The Logic of Priorities.

Only then can ASD ensure adequate and suitable facilities to support the mission of the 1990s and beyond.

## APPENDIX A

#### CURRENT ASD FACILITY PROBLEMS

This appendix presents by organization a tabulation of the current Aeronautical Systems Division (ASD) facilities that were found to be poor or marginal, i.e., were assigned grades of 1 or 2 on the scale given in Figure B-8 of Appendix B. The tabulation here lists those ASD facilities in Area "B" of Wright-Patterson Air Force Base for which adequate space (Section I), condition (Section II), suitability (Section III), and proximity (Section IV) problems exist. The criteria categories are defined in Table B-6 of Appendix B; the organizational acronyms are defined in a glossary at the end of this appendix.

TABLE A-1. FACILITY PROBLEMS: HEADQUARTERS

	ORGABIZATI		ASDCA	12001 12001	ABDCE	ASDTA	ASDTA							ATORA	ATORA	
ľY	BEILDIRG		=			:	=							•	<u>:</u>	
SUITABILITY	CATEGORY BEILDING ORGANIZATION	POBM/FIT	PLEXIBILITY				SEVI POSMEST	SERVICEABILITY	SPEC BONTS		PROXIMITY		# 1 - 1 - 2 - 2 - 2 - 2 - 2 - 2 - 2 - 2 -		DECTRI	
	CATEGORY			4.50CA 4.80CC	A 80CM	PROCE PROCE	<b>45</b> 014	ABDTA								
	MILDIBO			<b>=</b>		į	=	:								
CONDITION	C b 1 8 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	GRE STRECT	ETEC/MECS	SCOR LIFE				CHERGY								
	#OILT#XIEFDEC DEIGNIES LEODERS		49004	1400m	ASDCI ASDTA		45074	43064	0000	P 2000	ASDCE					
ADEQUACY OF SPACE	DEITOIRE		:		•		•	. :	:		•	!				
ACY	1	000108	ADMIN SPT			3PEC P03P	COMP ROOM	200000	;							

en encourage a production reserved products and encourage areased a recorded products and analysis. The safe

TABLE A-2. FACILITY PROBLEMS: ACQUISITION MANAGEMENT

AND DESCRIPTION OF STREET, AND STREET, AND

	CATROORY	P011-b180	OBCARISATION	C + 18	D011731100 086481341108	TOTATE DESCRIPTION	CATBODE:	BRITPIRG	115186 086481147104
100 1171 1171 1171 1171 1171 1171 1171	07710		110		- 5	11007	POBE/FIT		
100 100 100 100 100 100 100 100 100 100		: :	11017	ELEC/1000	<b>"</b>	1137		::	
					<u>.</u>		PLEXIBILITY	:	48840
10.10 10.10		ž			100			Ĉ	
	E	411,11	12021		2	1367		.:	200
		:=	1017	BCON LIFE	•••	200		20.20	
PROXIMITY		~ .			11,114	200		22.	
PROXIMITY			2017		:	318			
PROXIMITY		91 06	1007		;			n <b>-</b>	12:
PROXIMITY  Solve Service Servi		2 2 2	100		: ;			2 2 2	
PROXIMITY		<b>.</b> .	12021		2 -	1101		<b>3</b>	
### Control of the co		2 5 C	1981		ž. •	14001 1001	SERVICEABILITY	٠ ۾	
25		\$	1 2 2 2 2		. 2 3	1100		ž	11017
PROXIMITY  Solve to the state of the state o	•	5	2000		20.20v	2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	SPEC BONTS	**	148PH
PROXIMITY		12			12			185	
PROXIMITY  So to the control of the		Ê			<u> </u>			10% · 0%	
PROXIMITY  122 124 125 126 126 127 127 127 127 127 127 127 127 127 127	*	nr	1204 1204		ž	797		<u>.</u> .	11017
PROXIMITY  20, 100  2		<b>:</b>	# TI CT	F 0 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	w r-				
20, 20, 20, 20, 20, 20, 20, 20, 20, 20,		22 125	#4007 7007		11,114	7897 7897 7897 7897	PROX IMI TY		
22		. = '	# # # # # # # # # # # # # # # # # # #		<u>. 5</u>		:		
125		20.204	1101		*0.80x	1967	:	į	ORBARIZATION
125		2 2	12021		2 4 4		INTERORG	••	11004
15. 1.1.1.1.1.1.1.1.1.1.1.1.1.1.1.1.1.1.		58:	12024		S 4	12021		- 2	
25 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2		2	2007		*	1361		: <u>.</u>	
11. 11. 12. 120.00 11. 12. 120.00 12. 120.00 13. 120.00		•	12021					<u>.</u> .	1101
100 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1		•••	14007					5	1007
1994.7. 141. 141. 141. 141. 141. 141. 141.		11.11	1994					35.	11087
		=							
		!	200					n •-	1
12 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1		:	101					: :	
20 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2		22	11811					2 5	101
20 20 20 20 20 20 20 20 20 20 20 20 20 2		ž.	12051					•	
		, = :	# # # # # # # # # # # # # # # # # # #					=	
		20.20	100					70. 22 2. 22	12051
125 126 126 126 126 126 126 126		? <b>:</b>	13017					7 7 7	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1
****		126	4 3 3 E E					125	1984
		96.	1964					25	1000

PER 301 STS

TABLE A-3. FACILITY PROBLEMS: FUNCTIONAL MANAGEMENT

AND RESISSE THINKS THE PROPERTY OF THE PROPERT

DOILDING OBOANIESTION		504 48877		57 A 4 50 4 7 5 6	1	12 48017		55 A 588 A 5		193 ABST 139 ABST		100		193 4 48847			16 48911	11084	17087			504 ABDIT	
	FORM/FIT				PLEXIBILITY						RHVI BORMENT				SEBVICEABILITY		ALECT DEPT						
	11000 10000 10000 10000 10000	11917	12017	7 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	12011	7100	4 20 T 1	4 20 TT	7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7		A 500 A 4	17017	1001	11014	47077	3400	12011	19057	# 10 P P P P P P P P P P P P P P P P P P	1101	11011	4 40 4 4	
		55	2 22	≈ 2:	72	11,11	:22		- # !	2 2 2	50 ED 1			2	= 2	12:	% % % %	<b>3</b> :		<u>.</u>	- E	139	
CATGOORY	LUBBALM EMG		ELEC/MECS			RCOM LIPE																	
0804 M X M X M X M X M X M X M X M X M X M	4 2 5 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7	A1014 A5017	A 2011	7 P P P P P P P P P P P P P P P P P P P	A 4 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1		2507	4 1 2 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4	4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4	4 40 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	17081	1100	7 2 2 2 2	45077	12011	11011	27007	1 2011	12027	1987	12014	
98177880	4 4 8 8 8 8 8 8 8 8 8 8 8 8 8 8 8 8 8 8	11.114	<b>:</b> :	<b>9</b> 9 6	508	. n.	•	41,114	<b>9</b> p− (	228	4 2 5	ñ <b>3</b> .	ī <b>ā</b> ;	411.11	2 9			2:	::	9.	25	£ 5	;;
CA180087	101440	ADMIN SPT					29EC P019	COM ROOM						STOREGE									

PROXIMITY

TABLE A-4. FACILITY PROBLEMS: SPECIALIZED MANAGEMENT

populatesposos (massonal population) (populate (populate) (populate (populate)) (populate) (populate) (populate)

	A7108	<b>.</b>	<b>.</b>		IM 20-		
1 1 1 1 1 1 1	OBOARIE	1484		1001	M A A A A A A A A A A A A A A A A A A A	1	
Ϋ́	PULLDING	<b>2</b> 2:	- 55	= =	:	: =	
SUITABILITY	CATEGORI	PLEIBILITI		RN V I BORNE BT	SERVICE SELTT	SPEC BOSTS	PROXIMITY
CONDITION	CATROCAT BUILDING CROAMBALION		7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7 7	17007	17987 17987		
	BUILDING		::	23			
CONDITION	CATBOORT	BLEC/MECH	SCOS LIVE				
ADEQUACY OF SPACE	CATEGORY BELLETIES OF CATEGORY	7 4 8 8 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4			1 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	17077 77077 77077	4554L 4554T
ADEQUACY OF SPACE	<b>PB11D180</b>	7.	: 1			::	ñi
ADEQUACY	CATEGORY	ADMIN SPT		SPEC PORP	E000 4 8000	STORFOE	

CATROORY BOILDING OBSETTATION

ISTRAORG PES SUP BVS

TABLE A-5. FACILITY PROBLEMS: ORGANIZATION SUPPORT

CATROORI	BUILDIEG	08648134108	CATSGORY	80119180		7400AT43		
101440	-		ORB STREET	79.	40000	POBM/PIT	191	PORM/FIT 167 AEDDP
ADMIN SPT	•	1 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4	RIEC/MECH		# # # # # # # # # # # # # # # # # # #	PLEXIBILITY	444	2000 4 2000 4 2000 4
	411,114				- 4000 - 4000	MEVINOBART	1 6 7	18031
	:	7 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4	SCOR LIFE	•	1000 V	SERVICEABILITY	*	48004
	167	4850		11,114	1 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0		10	
SPEC PORP	191	43004		=	ASSTO	SPEC BONTS	2	48884 48884
	• 1.	43640		2	4 5010 4 5004		125	4000 T
CORF BOOM	•	1800E 1801G		92	A 30 80			
	111.11	4808P 4808C		125	48004	FINIAUG		
	. =	0 T B B T C		167	40004	FROALMLI		
	•	7 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	BBROT		# 4 5 0 0 E	CATROORY	BUILDIEG	BUILDING ORGARISATION
	125	4884 4888			0.004	LETREORO	-	ASDE
	: ;	OHORY		2				78010
	676	4200		125	ASSOF		125	10057
	•			167	43884		;	PROTO
	11.11	78057		56.	40084		56	19987
	9.	45010 48004					<b>e</b> Fe	7787
	10	750EV				INTRAORG	-	A 8 D D C
	125	ASDOP					125	18087
	167	ABDP					+95	70087
						PR 507 545	•	18001
							121	
								0100
							=	10024

FACILITY PROBLEMS: LABORATORIES TABLE A-6.

THE PROPERTY OF THE PROPERTY O

044 108	BEILDING	ORGANIZATION	CATEGORY	BOILDIBG	OBGARIZATION	CATEGORY	MILLING	BOLLVIIRVO
	223	MALAA	CHE STRUCT	24.244.8,	NALFI	BERNOT	14,1,	*****
	0 6 6	MALAA		59.594.B,C	WALFI		191	4414
	42	NAL T		200	TATE		7	
	Ē	MALFI		2	WALKL		06	MALAN
	0.64	UALKE		59,594,B,C	RALPO		079	WALAA
	18.184.8.0.0.8.0							ALLA
							3.0.425.25	
	}			22	MALAA		26	KALP I
ADMIR SPT	44.8.7	ATTA		2	WALAA		: =	14178
	22	NALAA		054	NALAA		\$ 7	NALP I
	222			120	44.4		59.594.B.C	ALL
	2			3 M . 24 . 25	14171		M	
				40.00.00.00	1414			MALPI
	622	MALA		. <del></del>	MALPI		161	TATE I
		MALAA		59.584.B.C	HALPI		192	I GTT TA
	24,244,8,0	MALFI		65,654	RALPI		255	RALPI
	25,254,B,C,D	NALP!		251	MALFI		984	RALFI
	92	UALFI		054	RALPI		20.20A	A LAL
	<u>.</u>	1170			ALL		200	
				Z0.Z0V				
	502	11111		s :			•	
							064	
	2 4			06.			3.4.2.5.6.6.	
	160			10, 10h. B.C. b. b. C.			*02.02	
								1
	16.184.8.C.B.E.G	MALPO		)			918	MALPO
		NALPO		41.4			- N	MALPO
	9	MALPO			1 T T T		9	WALPO
	5.7	PRAL		28.5	04148		0.50	TRAT
				064	04178			
SPEC PURP	223	44144		<b>S</b>	APUAL			
	0.0	44.4		D	7111			
	074			•	***			
	241	NALE I	177 100		1777			
	, ,	MALF			77172			
	054	MALKI		223	MALAN			
		MALPO		<b></b>	44144			
	450	MALPO		-24	MALAA			
				24,244,B,C	MALFI			
COMP ROOM	44.B.F	AALAA		25,254.B,C.D	MALFI			
	22	WALAA		*	MALPI			
	228	MALAA		<b>.</b>	WALF			
	N							
				7, 3, 24, 10,				
	233	MALAA		159.39	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1			
		*****						
	24.24A.B.C	MALP		~~-	KALPI			
	25,254,8,0,0	MALFI		20,204	BALML			
	32	RALPI		25	MALML			
	÷ M	I TT T		5	RALML			
	6	1 2 1 2 1 2 1		•				
	25.6	NALP1		16.184.8.C.D.E.O	NALPO			
	255	MALFI		20,204	MALPO			
	0 10 10	NALT.		2.2	MALFO			
	25.			59, 594, B, C	WALPO			
	9 0	1212		•				
	18, 184. B.C. D. B.C	MALPO		4	MALPO			
		MALPO		252	MALPO			
	• 30	MALPO		<b>57</b>	APUAL			

TABLE A-6. FACILITY PROBLEMS: LABORATORIES (Continued)

POBM/FIT	BOILDIRG	CHOANIZATION	CATEGORY	CATEGORY BUILDING ORGANIZATION		CATEGORY	BOILDIRG	OBOARIZATION
PLEEZELLTT			SPEC BONTS	25, 25, 25, 25, 25, 25, 25, 25, 25, 25,		0.00	4 5 4 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5 5	
	24, 24, 24, 24, 24, 24, 24, 24, 24, 24,			4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4	######################################	2 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	450 450 186 186 186 186 186 186 186 186 186 186	
	24 B. P. 24 B. C. 25					99 AD 60 61 64		

# GLOSSARY OF ORGANIZATIONAL COMPONENT ACRONYMS

	ASD	Agranautical Systems Division
		Aeronautical Systems Division
C.	WAL	Wright Aeronautical Laboratories
<del>9</del>	AA	Avionics Laboratory
3	AC	Comptroller
	AD	Computer Center
Υ <u>ς</u>	AE	Deputy for Aeronautical Equipment
ē,	AF	Deputy for Airlift and Trainer Systems
	AL	Acquisition Logistics
<u> </u>	AV	Assistant for Acquisition Management
Š	AW	Deputy for Acquisition Support
	AX	Deputy for Avionics Control
3	B1	Deputy for B-1B
	ВС	Small and Disadvantaged Business Utilization Office
8	CA	Equal Employment Opportunity Office
	CC	Commander
	CM	Senior Enlisted Advisor
Ŷ.	CS	Chief of Staff
Č.	cv	Vice Commander
	CX	Secretariat
	DA	Directorate of Administration
ъ. Ф.	DE	Research and Development Civil Engineering
2	DP	Personnel
	EN	Deputy for Engineering
	FI	Flight Dynamics Laboratory
ر. بر ب	НО	History Office
	IG	Inspector General
	ML	Materials Laboratory
	PA	Office of Public Affairs
ž	PM	Deputy for Contracting and Manufacturing
ğ	PO	Propulsion Laboratory
	RW	Deputy for Reconnaissance/Strike and Electronic Warfare Systems
Š.	SE	Safety Office
	**	•
		A-9
<b>7</b> 5.		·· ·

SP	Security Office
TA	Deputy for Tactical Systems
WE	ASD Staff Meterological Office
XO	Administrative Airlift Plans and Operations Division
XR	Deputy for Development Planning
YP	Deputy for F-16
YW	Deputy for Simulators
YY	Deputy for Strategic Systems
YZ	Deputy for Propulsion

#### APPENDIX B

#### EVALUATION OF EXISTING CONSTRUCTION ALTERNATIVES

In seeking solutions to current and future Aeronautical Systems Division (ASD) facility problems, the following five proposed alternatives were considered:

- No construction;
- Building addition to consolidate Deputy for Engineering (EN) functions;
- Addition to the Avionics Laboratory;
- Addition to the Flight Dynamics Structures Test Facility; and
- Construction of a Systems Management Engineering Facility (SMEF).

The construction alternatives were those specified in the five year MCP submittal. In order to evaluate these alternatives, LMI developed a method of quantifying the benefits of each. The alternatives were compared to determine the best combination of projects, and that comparison was used to formulate the final Facilities Management Plan.

This appendix describes each alternative, the evaluation procedure, and the results of the comparison. Two annexes are presented to show the quantitative results of the evaluation.

# NO CONSTRUCTION

Many facilities improvements can be made in Area "B" without new construction. Minor construction, alterations, rehabilitations, relocations, and improved utilization will help to moderate the effects of current facility problems at ASD. Table B-1 illustrates only a few of the "no-construction" possibilities. The improvements listed in Table B-1 are worthwhile and should be pursued as part of a comprehensive long-term Facilities Management Plan.

However, in themselves, they are not sufficient to alleviate the overal. ASL problems. The additional space required cannot be provided through alterations and relocations alone. The suitability of a 40-year-old warehouse for modern technical research and development (R&D) work cannot be materially effected through rehabilitation projects. Those outmoded facilities, which are 40-, 50-, or 60-years-old, will eventually have to be replaced regardless of how much money is spent upgrading them. Even the proximity issue (described in Chapter 2 of the main text) cannot be solved solely through relocation; there are too many small buildings in Area "B" to allow consolitation, at even the lowest organizational level.

TABLE B-1. SOME "NO-CONSTRUCTION" POSSIBILITIES

BUILDING	ACTION
821	Move Avionics Laboratory (AA) personnel out.
4A	Assign AA personnel from Building 821.
24C, Area"C"	Move Flight Dynamics (FI) personnel out.
1, 9	Assign FI personnel if proposed Air Force Museum
	Military Construction Project (MCP) is implemented;
	assign EN personnel from Building 125.
7	Assign EN personnel from Building 125 it Air Force
	Museum MCP is implemented.
6, 22	Assign FI personnel if Air Force Museum MCP is not implemented.
254	Rehabilitate for Gas Dynamics or other group
167	Move Personnel Office out; assign to Source
	Selection.
126	Move EN personnel out; install Personnel Office
125	Move Source Selection out; assign to EN personnel
450	Move Avionics Laboratory (AA) and Material Labora-
	tory (ML) personnel out; building ready for
	reassignment.
620	Assign AA personnel from Building 450.
652	Assign ML personnel from Building 450.

Thus, the "no construction" alternative was judged not feasible as a stand-alone solution. However, several individual modifications, relocations.

etc., were incorporated into the development and evaluation of the four construction alternatives.

## DEPUTY FOR ENGINEERING CONSOLIDATION

A \$30 million MCP proposed for FY87 would consolidate the EN functions by constructing a 250,000 square foot addition to Building 485. The proposed project would result in consolidation of all EN functions and personnel in one expanded building. As currently scoped, the project would provide a central EN simulation facility for five simulators and 60,000 square feet of special access space for highly classified requirements.

As a result of this project, some space (approximately 123,000 square feet: would become available in Buildings 6, 11, 16, 20, 22, 46, 56, and 125 and Buildings 28A, 126, and 156 would be completely vacated. The proposals for disposition of the vacated space are shown in Table B-2. In the evaluation, the proposed relocations were considered to be a significant benefit of the project

TABLE B-2. DISPOSITION OF SPACE VACATED BY PROPOSED MCP FOR CONSOLIDATION OF EN FUNCTIONS

IN BUILDING 485

BUILDING	ACTION
b	Office space for FI.
11,16,20,	Additional space for special project offices (SPOs)
22,46,56	for YY, YZ, TA, AE, and AF <sup>a</sup> .
28A, 156	Demolish.
126	Office space for Personnel Office.
125	Office space for Source Selection; short-term quarters
	for Air Force Institute of Technology (AFIT); space
	for Defense Institute of Security Assistance Manage-
	ment (DISAM); possible space for technical library.

Tactical Systems; AE: Deputy for Aeronautical Equipment; AF: Deputy for Airlift and Trainer Systems.

#### AVIONICS LABORATORY ADDITION

The addition to the Avionics Laboratory (Building 620), as proposed for the MCP, would provide 133,537 square feet (gross) of R&D and office space at a cost of \$15.9 million. It would house a new consolidated electro-optics laboratory and also provide space for development of combat digital evaluation technology, a recently imposed ASD requirement. In addition to collocating 90 percent of the Avionics Laboratory personnel, the project would improve utilization of existing high-cost laboratory space in Building 620 that must currently be used as office space. This project is currently carried in the FY87 MCP.

The major secondary benefit of the proposed project would be an 87,000 square foot reduction in total Avionics Laboratory inventory and the release of substantial amounts of space in Buildings 22, 22B, 622, and 739. Table B-3 shows the proposed uses for this available space. As with the EN project, the benefits from proposed moves were considered in the evaluation of the Avionics Laboratory addition.

TABLE B-3. DISPOSITION OF SPACE VACATED BY PROPOSED MCP FOR AVIONICS LABORATORY ADDITION

BUILDING	ACTION
22,22B	Vacated by Avionics Laboratory; available to FI personnel from Buildings 24B, 31, 45, 63, 93, 191, 461.
Area "C"	Vacate FI components (Tire Testing Laboratory and Lightning Strike Laboratory).
622	Storage or demolition.
739	Demolition.

## STRUCTURES TEST FACILITY ADDITION

The \$13.9 million proposed project for an addition to the Flight Dynamics Structures Test Facility would add 64,800 gross square feet to Building 65.

This FY87 MCP would allow consolidation of the Structures and Dynamics Division of the Flight Dynamics Laboratory and provide improved computer capability to support its work.

Because the scope of this project is small, the secondary effects are limited. As shown in Table B-4, some space would become available in Buildings 24C and 461. These effects were considered in the evaluation of this alternative.

TABLE B-4. DISPOSITION OF SPACE VACATED BY PROPOSED MCP FOR ADDITION TO FLIGHT DYNAMICS
TEST FACILITY

BUILDING	ACTION
24C	Administrative offices available for other FI components.
461	Standby status.
65	Establish central computer facility.

## SYSTEMS MANAGEMENT ENGINEERING FACILITY

The SMEF, as originally conceived, would be a new 250,000 square foot facility to house the SPO organizations. This \$27 million project was originally proposed as part of the FY88 MCP program. In reviewing requirements and possible alternatives, the size was raised to 330,000 square feet and the cost to \$33 million for purposes of evaluation.

The proposed project would provide adequate and suitable space for all SPO organizations in a consolidated facility near the headquarters and support organizations. The new facility would also provide flexibility for accommodating changes in the SPOs without adversely affecting other organizations. Much of the space vacated as a result of this project would be recommended for demolition, which would ease traffic and congestion problems in

Area "B." As shown in Table B-5, some space would also be available for a partial consolidation of EN functions. As with the other alternatives, these secondary effects were considered as part of the benefits for the proposed project.

TABLE B-5. DISPOSITION OF SPACE VACATED BY PROPOSED MCP FOR SMEF CONSTRUCTION

BUILDING	ACTION
11,11A,16 28	House EN functions. House AMRL (Eliminate FY88 Aerospace Medical Research Laboratory (AMRL) MCP).
126	Office space for Personnel Office.
125	Office space for Source Selection.
17,28A,30, 31,32,36, 38,51,56, 57,156, 190,196, 197,198, 434	Demolish.

# **EVALUATION PROCEDURE**

In order to evaluate the four construction alternatives objectively, a method was needed to quantify the benefits of each for comparative purposes. The first step in this process was the establishment of evaluation criteria. Table B-6 lists the criteria used and gives a brief definition of each. Since some of these criteria are more important than others, values had to be established for the criteria for each ASD functional group. These values were established using the Analytic Hierarchy Process<sup>1</sup> to determine relative priorities or levels of importance. The process is based on pair-wise comparisons of the different criteria from which numerical values or weights are

<sup>&</sup>lt;sup>1</sup>Dr. Thomas L. Saaty, <u>The Analytic Hierarchy Process</u> (McGraw-Hill, Inc., New York, 1980).

#### TABLE B-6. DEFINITIONS OF EVALUATION CRITERIA

ADEQUATE SPACE - Square footage required to house the function. Use standards for judgment.

OFFICE - Space required to house personnel, engineers, scientists, managers, and administrators.

ADMIN. SUPPORT - Space required to support administrative functions; duplication rooms, central files, reception areas, etc.

SPECIAL-PURPOSE SPACE - Nonstandard space required by the mission; laboratory, engineering, and test space, shops classified areas, etc.

CONFERENCE ROOM - Space required for team work sessions, conferences, group discussions, etc.

STORAGE - General storage space for noncurrent records, consumables supplies, etc.

CONDITION - Building integrity; limitations of buildings system.

GENERAL/STRUCTURAL - General condition of building envelope, soundness.

ELEC/MECHANICAL - Condition of standard building power and heating, ventilation, and air conditioning (HVAC) systems.

ECONOMIC LIFE - Remaining useful life of the building, investment potential, worth.

ENERGY - Efficiency index of energy usage for the building.

SUITABILITY - Appropriateness for the mission.

FORM/FIT - Configuration; efficiency of utilization; internal traffic pattern; work flow; structural layout.

FLEXIBILITY - Ability to accommodate change.

ENVIRONMENT - Impact of building surroundings on morale; productivity factors.

SERVICEABILITY - Capability for service; accessibility; parking, etc.

SPECIAL REQUIREMENT - Nonstandard utilities/equipment/hardware to support mission; safety/security/data/material handling/toxic waste/special power, etc.

<u>PROXIMITY</u> - Closeness to other buildings/functions; ease of travel/interaction; ease of technology transfer.

INTERORGANIZATIONAL INTERFACES - Position in relation to other units within command and other organizations; geographical location on the base; adjacent buildings; available land; base utilities and traffic.

INTRAORGANIZATIONAL INTERFACES - Chain of command/management control; organizational integrity/relationships. outside interfaces; ease of communication/technology transfer.

PERSONNEL SUPPORT SERVICES - Availability of support services, i.e., cafeteria, personnel office, post office, bank exchange, etc.

calculated. Table B-7 shows the average values and ranges of values established for the evaluation criteria. The range reflects the fact that the values were actually set through consultation with managers from the seven major ASD organizational groups located in Area "B" and that the specific values vary among the groups. Annex 1 to this appendix shows the values by organizational group.

TABLE B-7. EVALUATION CRITERIA VALUES

CRITERION	RANGE	AVERAGE
Adequate space	44 - 121	63
Condition	17 - 21	18
Suitability	51 - 118	107
Proximity	7 - 19	72
TOTAL VALUES		200

With criteria and values established, the last step was to measure the effectiveness of each alternative in meeting the criteria. The effectiveness was measured through a scoring process that graded each organization in each facility. A grading scale was established as shown in Table B-8, and each facility was evaluated on the basis of its usefulness to the organizations housed in it. A score was computed by multiplying the criterion value by the grade. Table B-9 illustrates this process for one organization and building. Complete tabulations of the scores for the current situation and each alternative are given in Annex 2 to this appendix.

## **EVALUATION RESULTS**

The results of the evaluation for the four construction alternatives are displayed in Table B-10 along with the score for the base case (the current situation). The numbers across the rows reflect the scores for each

TABLE B-8. GRADING SCALES FOR EVALUATION CRITERIA

		C	RADING SCA	LE	
CRITERION	1	2	3	4	5
ADEQUATE SPACE					
Office	<u>+</u> 20	<u>+</u> 15	<u>+</u> 10	<u>+</u> 5	90
Admin. Support	10	15	20	25	30
Special Purpose	Poor	Marginal	Adequate	Good	Superior
Storage	1%	2.5%	5%	7.5%	10% Gross
Conference Room	Poor	Marginal	Adequate	Good	Superior
CONDITION					
Gen./Struc.	3		2		1
Elec./Mech.	Poor	Marginal	Adequate	Good	Superior
Energy	Poor		Adequate		Superior
Econ. Life	40	30-40	20-30	10-20	New
SUITABILITY					
Form/Fit	Poor	Marginal	Adequate	Good	Superior
Sp. Rqmts.	Poor	Marginal	Adequate	Good	Superior
Serviceability	Poor	Marginal	Adequate	Good	Superior
Flexibility	Poor	Marginal	Adequate	Good	Superior
Environment	Poor	Marginal	Adequate	Good	Superior
PROXIMITY					
Interorg. Interface	Remote from 2&3	Remote from 3s	Near some 3s	Near all 3s	Near 2&3s
Intraorg. Interface	20-30%	15-20%	10-15%	5-10%	5% out- side zone
Pers. Suppt. Services	Remote		Average		Near

TABLE B-9. SAMPLE EVALUATION OF ACQUISITION MANAGEMENT ORGANIZATIONS

IN BUILDING 11/11A

CATEGORY	VALUE	GRADE	SCORE
Adequate Space Office Administrative Support Special Purpose Conference Room Storage	48	5	240
	52	1	52
	11	3	33
	6	2	12
	4	5	20
Condition  General/Structural  Electrical/Mechanical  Economic Life  Energy  Suitability	8 11 1	3 4 1 2	24 44 1 2
Form/Fit Flexibility Environment Serviceability Special Requirements	15	4	60
	25	3	75
	3	4	12
	4	4	16
	4	4	16
Proximity Interorganizational Intraorganizational Personnel Support Services	1	5	5
	6	4	24
	0	5	0
Organization/Building Total MAXIMUM VALUES	200	<b></b> 5	636 1000

alle passers, parador decesso recocción decisión estador despesa despesa estador passessão dependada per

organizational group for each alternative, while the bottom line shows the average ASD score for each alternative.

The EN project, as expected, has the most significant impact in the Functional Management group with minor improvements in the Acquisition Management, Specialized Management, and Organizational Support. The increase in the overall ASD score for this alternative shows significant improvement.

The Avionics Laboratory project results in significant improvements for both the Avionics Laboratory and the Flight Dynamics Laboratory. This is a

TABLE B-10. RELATIVE BENEFITS OF FOUR CONSTRUCTION ALTERNATIVES

ORGANIZATIONAL GROUP	BASE CASE	ENª	AA	FI	SMEF
Headquarters	620	620	620	620	641
Acquisition Management	467	510	481	467	749
Functional Management	572	617	572	572	652
(EN)	(546)	(719)	(546)	(546)	(717)
Specialized Management	533	570	533	533	614
Organizational Support	598	623	598	598	617
Laboratories					
AA	514	514	608	514	514
FI	537	544	567	539	544
ML	613	613	613	613	613
PO	572	579	572	572	577
ASD Average Score	552	574	558	552	621

<sup>a</sup>KEY: EN: MCP for consolidation of EN functions.

AA: MCP for addition to Avionics Laboratory.

FI: MCP for addition to Flight Dynamics Structures Test

Facility.

SMEF: MCP for construction of SMEF.

result of the large amounts of space that would become available for Flight Dynamics use as a result of this project. The impacts of the proposed project outside of the laboratories are minor, but the overall increase in the ASD score is a significant improvement for a project of limited size and scope.

The Flight Dynamics alternative reflects limited improvements for the Flight Dynamics Laboratory, and no improvement for any other group or for ASD as a whole. Even in terms of total Flight Dynamics requirements, this project does not offer as much as the Avionics Laboratory alternative. This result

does not mean that the project is not a valid one for the Structures and Dynamics Division. However, it is so limited in scope that it does not have an impact on the larger facilities picture. Furthermore, it appears that the Structures and Dynamics requirements could be accommodated in buildings vacated by the Avionics Laboratory as a result of its proposed MCP. These buildings are adjacent to Building 65 and would offer a viable alternative. However, major modification and improvement would be required.

The SMEF construction offers the largest overall improvement in ASD facilities, while providing major improvements for every organizational grouping except the laboratories. This alternative raises the score for EN almost as much as the EN MCP.

#### DISCUSSION


Table B-11 shows the relative benefits, or improvements, of each project reflected against the cost of the project. While these figures are important, they do not tell the whole story. In order to put these figures in perspective, it is necessary to review the base case or current situation. Figure B-1 shows the distribution of current scores for the various organizational groups. Acquisition Management has the lowest average score, followed by Avionics Laboratory, Specialized Management, Flight Dynamics Laboratory, and the Deputy for Engineering. Based on these figures, the SMEF project would appear to be a good choice since it would solve the Acquisition Management, Specialized Management, and EN problems. However, it would not address serious problems in the laboratories. The EN alternative would have similar impacts. For these reasons, the laboratory projects may be required as additions or supplements to the EN or SMEF projects.

TABLE B-11. RELATIVE BENEFITS AS A FUNCTION OF COST

1	EN	AA	FI	SMEF
MCP Cost (\$M)	30.0	15.9	13.4	23.0
Benefit <sup>a</sup>	570(+18)	558(+6)	552(0)	621 (+69)
Cost/Benefit (\$M)	1.67	2.65		0.30

 $<sup>^{\</sup>mathrm{a}}\mathrm{ASD}$  average score (increase over base case).

FIGURE B-1. WPAFB-B/ASD - BASE SCORING SUMMARY

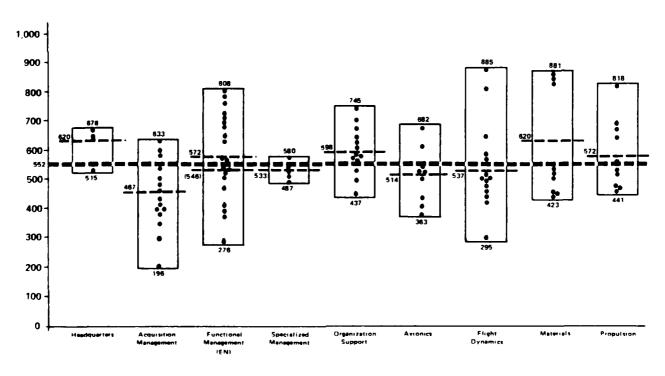

ASD Average
Organization Average

Table B-12 shows scores for the various projects in combination. Since the EN and SMEF projects have considerable overlap in terms of requirements and results they were not considered in combination. The benefits of all other projects were considered to be additive for the purposes of analysis. The analysis shows that the proposed Avionics Laboratory MCP in combination with either the SMEF or EN MCP would be the best alternatives in terms of correcting major ASD deficiencies. Although the Flight Dynamics/SMEF combination scores higher than the EN/Avionics Laboratory combination, this result is artificial because the score would be the same without the Flight Dynamics MCP. As already noted, however, the SMEF MCP cannot stand alone because it leaves too many problems unsolved for the laboratories.

#### RESULTS

Of the four construction alternatives reviewed, we judged three to be cost-effective for ASD. They are

- Consolidation of EN functions;
- Avionics Laboratory addition;
- SMEF construction.

However, all three MCPs cannot be justified as currently proposed. Because of the overlap between the EN and MCPs, the scope of one or the other or both of these projects needs to be decreased. Since the SMEF MCP has a better payoff than the EN MCP and solves most of the EN problems, it should be left basically unchanged. It could, however, be phased in order to spread the costs over two years. The EN MCP should be substantially reduced in scope to accommodate only those requirements not provided for through the secondary effects of the SMEF project. The Avionics Laboratory MCP is generally acceptable at its current level.

TABLE B-12. RELATIVE BENEFITS OF COMBINING PROJECTS

ORGANIZATION- AL GROUP	BASE CASE	EN/ AA <sup>a</sup>	EN/ FI	AA/ FI	AA/ SMEF	FI/ SMEF	EN/AA/ FI <sup>b</sup>	AA/FI/ SMEF
Headquarters	620	620	620	620	641	641	620	641
Acquisition	467	524	510	481	749	749	524	749
Functional Management (EN)	572 (546)	617 (719)	617 (719)	572 (546)	652 (717)	652 (717)	617 (719)	652 (717)
Spec. Mgt.	533	570	570	533	614	614	570	614
Organization- al Support AFWAL	598 514	623 514	623 514	598 514	617	617 514	623 514	617 514
Labs	559	594	563	591	593	563	594	593
(AA)	(514)	(608)	(514)	(608)	(608)	(514)	(608)	(608)
(FI)	(537)	(574)	(546)	(569)	(574)	(546)	(576)	(574)
(ML)	(613)	(613)	(613)	(613)	(613)	(613)	(613)	(613)
(PO)	(572)	(579)	(579)	(572)	(577)	(577)	(579)	(577)
ALL ASD	552	580	574	558	626	621	580	626

<sup>&</sup>lt;sup>a</sup>KEY: EN: MCP for consolidation of EN functions.

The timing of the projects -- which goes first, second, or third -- is dependent on funding levels and design time. The Avionics Laboratory and EN projects are already in preliminary design, which means they should probably precede the SMEF project.

AA: MCP for addition to Avionics Laboratory.

FI: MCP for addition to Flight Dynamics Structures Test Facility.

SMEF: MCP for construction of SMEF.

<sup>&</sup>lt;sup>b</sup>Combinations including EN and SMEF together were not considered because of the substantial overlap between the projects.

These three projects form the core of a long-term plan. However, other moves, modifications, demolitions, etc., that support the planning concepts should proceed along with these MCPs. Other MCPs, such as a final consolidation for Flight Dynamics and a replacement for the Propulsion Laboratory should also be considered now as part of a long-term plan.

Details of size, scope, location, occupants, etc., will have to be developed as the planning process proceeds, and adapted as conditions require. However, these MCPs, as revised, provide a solid framework for all future detailed planning.

# ANNEX 1

# EVALUATION CRITERIA ASSIGNED VALUES

This annex presents the values established for the criteria (given in Table B-6 of this appendix) for each ASD organizational group. A glossary of the organizational acronyms used in this annex is presented at the end of Appendix A.

ORGANIZATIONAL	CATEGORY	VAL	JES
GROUP		ITEM	TOTAL
ASD/ HEADQUARTERS	ADEQUATE SPACE  Office Administrative Support Special Purpose Conference Room Storage	22 11 3 18 3	57
	CONDITION  General/Structural Electrical/Mechanical Energy Economic Life	7 8 1 1	17
	SUITABILITY  Form/Fit Flexibility Environment Serviceability Special Requirements	29 4 8 71 4	116
	PROXIMITY  Interorganizational Intraorganizational Personnel Support Services	3 7 0	10
SPECIALIZED MANAGEMENT	ADEQUATE SPACE  Office Storage Conference Room Administrative Support Special Purpose  CONDITION	24 10 1 20 3	58
	General/Structural Electrical/Mechanical Energy Economic Life	7 8 1 1	
	SUITABILITY  Form/Fit Flexibility Environment Serviceability Special Requirements  PROXIMITY	28 4 8 71 4	115
!	Intraorganizational Interorganizational Personnel Support Services	1 8 1	10

ORGANIZATIONAL	CATEGORY	VAL	UES
GROUP		ITEM	TOTAL
ACQUISITION MANAGEMENT	ADEQUATE SPACE Office Administrative Support Special Purpose Conference Room Storage	48 52 11 6 4	121
	CONDITION		21
	General/Structural Electrical/Mechanical Energy Economic Life	8 11 1 1	
	SUITABILITY		51
	Form/Fit Flexibility Environment Serviceability Special Requirements	15 25 3 4 4	
	PROXIMITY		7
	Interorganizational Intraorganizational Personnel Support Services	1 6 0	
FUNCTIONAL MANAGEMENT	ADEQUATE SPACE  Office Administrative Support Special Purpose Conference Room Storage	25 7 3 23 1	59
	CONDITION  General/Structural  Electrical/Mechanical  Energy  Economic Life	7 8 1	17
	SUITABILITY	· ·	116
	Form/Fit Flexibility Environment Serviceability Special Requirements	33 58 7 10 8	-10
) 	PROXIMITY		8
: , , ,	Interorganizational Intraorganizational Personnel Support Services	1 7 0	

ORGANIZATIONAL	CATEGORY	VAL	JES
GROUP		ITEM	TOTAL
DEPUTY FOR	ADEQUATE SPACE		44
ENGINEERING	Office Administrative Support Special Purpose Conference Room Storage	8 3 24 8 1	
	CONDITION		19
	General/Structural Electrical/Mechanical Energy Economic Life	13 1 1	
	SUITABILITY		118
	Form/Fit Flexibility Environment Serviceability Special Requirements	13 22 4 6 73	
	PROXIMITY		19
	Interorganizational Intraorganizational Personnel Support Services	3   15   1	1
ORGANIZATIONAL SUPPORT	ADEQUATE SPACE Office Administrative Support Special Purpose Conference Room Storage	25 22 3 1 7	58
	CONDITION		17
	General/Structural Electrical/Mechanical Energy Economic Life	7 8 1 1	
	SUITABILITY		116
	Form/Fit Flexibility Environment Serviceability Special Requirements	33 58 7 10 8	
	PROXIMITY		9
	Interorganizational Intraorganizational Personnel Support Services	1 8 0	

ORGANIZATIONAL	CATEGORY	VALU	JES
GROUP		ITEM	TOTAL
LABORATORIES	ADEQUATE SPACE		45
	Office Administrative Support Special Purpose Conference Room	6 1 32 6	
	CONDITION		18
	General/Structural Electrical/Mechanical Energy Economic Life	3 13 1 1	
	SUITABILITY		118
	Form/Fit Flexibility Environment Serviceability Special Requirements	57 6 14 17 24	
	PROXIMITY		19
	Interorganizational Intraorganizational Personnel Support Services	15 3 1	

#### ANNEX 2

#### **EVALUATION RESULTS**

This annex presents the results of the quantitative evaluation of the effectiveness of each criterion specified in Table B-6 of this appendix. Complete tabulations of the scores for the current situation (base case) and each alternative are given in this annex. The alternatives are:

- Alternative 1: a 250,000 square foot addition to Building 485 for EN functions;
- Alternative 2: a 134,000 square foot addition to Building 620 for the Avionics Laboratory;
- Alternative 3: a 65,000 square foot addition to Building 65 for the Flight Dynamics Laboratory; and
- Alternative 4: a new 250,000 square foot building to house the Systems Program Office (SPO).

A glossary of the organizational acronyms used in this annex is presented at the end of Appendix A.

FACILITY EVALUATION SCORES FOR THE BASE CASE

ASD AVERAGE SCORE: NUMBER OF ENTRIES:

ORGANIZATIONAL GROUP	BUILDING	ORGANIZATION	SCORR	ORGANIZATIONAL GROUP	BUILDING	ORGANIZATION	SCORE
		ASDCA	624	ORGANIZATION SUPPORT		ASDDE	\$12
	. =	0000	633		•	1 1 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	
	: =	NO CONT	200		•	9 4 6 9 4	919
		80084	W 12		11. 11		E 43
	7	ASDCV	6.33		•	ONON	785
	=	ASDCK	624			ASDPA	634
	188	ASDTA	515		=	ASDKO	669
ACQUISITION MANAGEMENT	11,114	ASDIA	200		9 ;	ASDDA	605
	2 :	4004			<u>•</u>		200
	5 9	41004	6.00		125		57.5
	. 9	ASDIT	984		125	PROTO	165
	9.	ASDIE	547		167	ASDDP	437
	11	ASDAF	•		195	ASDDA	0 17 9
	22	ASDAR	200			ASDAD	268
	<b>5</b>	BELON V	95	LABONATORIES	F. B. S.	41.42	545
•	•	7100	293		302		126
	90	11001	- 64		200	44.43	21.4
	25	A SOB	=		23	44142	25
	22	ASDA	413		120	MALAA	
	26	ASDAF	545		620	HALAA	682
	51	ASDAE	473		622	MALAA	777
	-6	ASDAF	462		821	WALAA	598
	193	ASDIT	507		24,244-0	MALFI	510
100000000000000000000000000000000000000	42.5	M 4 200 4	9 4		., ,		<b>2</b>
	n r	1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1 1	9 4		9 5	14171	0 e
	11,114	2004	683		- 5		4 t
	11,11	ASDIR	799		59.594-0		521
	-	ASDAC	678		'n	WALFI	14.4
	=	ASDPM	623		65,654	WALPI	620
	=	ASDIR	150			NALFI	524
	9 :	Z COA	525		54.	I ATE	170
	<b>e</b> :	A SA	532		•	TATES	90
	7.4	ASDXB	8 90		192	T T T T	20.00
		ASDRE	545		254	WALFI	295
	=	ASDER	200		255	WALFI	559
	<b>3</b>	ASDER	617		150	WALFI	454
	20,204	RECOVE.	379		_	WALFI	664
	28.4				32,03	E PERE	8 2 C
	9	N N N N N N N N N N N N N N N N N N N	715			MALMI	517
	125	ASDER	412		26	WALML	452
	126	ASDEN	904		414	WALML	423
	156	ASDER	276		ĸ.	MACHE	427
	502	A SOL	9		•	ALAL.	20 0
SPECIALIZED RAMAGEMENT	<u></u>	A COP	0 4		250	AALAL	999
	2 4	PACO T	- ec		19 194-1 0		100
	9 0	14084	2.5		20.204		65.0
	26.	ASSOR	532		; 	0 4 1 ≥ 0	989
					59,594-C	WALPO	524
					7	WALPO	994
					41.	WALPO	545
					8 . · ·		9 10
					710		25 25 26 26 26 26 26 26 26 26 26 26 26 26 26
					202		
					0 G	DATE A	- «
					) (1)	APER I	9
					150	APWAL	532

S Socoli epedebli Socordoli especient especient ( especient ( especiente) especiente ( especiente) especiente ( e

OBGENITATIONAL GROUP	FOR AL	FOR ALTERNATIVE #1	ASD AVERAGE NUMBER OF EN	SCORE: 574 TRIES: 109		
adogarters Adogarters	BOILDING	NO	GCORE ORGANIZATIONAL GROUP		BUILDING	ORGANIZATION
ACQUISITIOM MANAGEMENT	14 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4 4	ASUCA ASUCCA ASUCCA ASUCCA ASUCA ASUCA ASUCA ASUCA ASUCA ASUCA ASUCA ASUCA ASUCA ASUCA	624 ONGANIZATION SUPPORT 633 678 633 624 624 515 770 770 770 770			4444444444
		1004 1004 1009 1009 1009 1009 1009 1009	701 656 659 688 688 888 884 841 413 413 862 507	2010 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2 2	7 126 B	A SOUP PER PROPERTY NAMED POR PORTION PROPERTY NAMED PORTION PROPERTY NAMED PORTION PROPERTY NAMED PROPERTY NAM
FUECTIONAL MANAGEMENT	739 7 11,114 11,114 14,114 14 16 16 16 125/167	PRODER PR		2	24(/6) 25,254-D 31 31 35,594-C 59,594-C 146 191 191 254	REPLIENT THE STATE OF THE STATE
NAME TALILY NO. TAREAGNER NEW THE NAME OF	\$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$ \$	E A P G G G G G G G G G G G G G G G G G G	933 839 1 6 839 1 6 839 1 6		255 #50 #50 20,20A 51 51 55 652 652 652 652 652 652 714 718 718 718 718 718 718	KAPILPO KAPILP

FACILITY EVALUATION SCORES
FOR ALTERNATIVE #2

ASD AVERAGE SCORE: NUMBER OF ENTRIES:

THE POWER PROPERTY OF THE PARTY AND THE PROPERTY PROPERTY CONTRACTOR TO THE PARTY AND THE PARTY.

A SUBSTITUTE OF THE STREET OF THE SUBSTITUTE OF 18,164-K,G,B 20,204 21 BUILDING 24,244-C 25,254-D 29,594-C 55,654 ORGANIZATIONAL GROUP ORGANIZATION SUPPORT LABORATORIES SCORE OBGARIZATION BUILDING 11,114 411.11 \$0,20A ORGANIZATIONAL GROUP ACQUISITION NAMADENENT SPECIALIZED MANAGEMENT PUNCTIONAL MANAGEMENT HEADQUARTERS

# FACILITY EVALUATION SCORES FOR ALTERNATIVE #3

ASD AVERAGE SCORE: NUMBER OF ENTRIES:

スペイン

Seconds Markey Stranger Branch Branch Branch

18, 184-E, G, B BUILDING 24,244-C 59,594-C 63 55,65A 20,20A ORGANIZATIONAL GROUP ORGANIZATION SUPPORT LABORATORIES SCORE ORGANIZATION BUILDING 10,204 ORGANIZATIONAL GROUP SPECIALIZED MANAGEMENT ACQUISITION MANAGRMENT FUNCTIONAL MANAGEMENT HEADQUARTERS

9,59A-C

FACILITY EVALUATION SCORES
FOR ALTERNATIVE #4

626 113

ASD AVERAGE SCORE: NUMBER OF ENTRIES:

	ORGANIZATIONAL GROUP	BUILDING	ORGANIZATION	SCORE	ORGANIZATIONAL GROUP	BOILDING	ORGANIZATION	SCORE
1		•	ASDCA			80		512
1		. A.C.	ASDCC	623		. 00	DIOS	533
1		- <del>-</del>	ASDCH	633		. 00	ASDSP	919
1, 11, 11, 11, 11, 11, 11, 11, 11, 11,		<b>?</b>	A SDCS	678		11.114	ASDBC	563
10		=	ASDCV	633		11,114	ASDKO	745
1, 11, 1, 1, 1, 1, 1, 1, 1, 1, 1, 1, 1,		**	ASDCK	624		<b>=</b>	ASDPA	<b>₹</b> €9
		168/14	ASDIA	661		*	ASEKO	669
	ACCOLSTICE NAMEDERNAL	11,114/3865		9 4		9 4		0 4
		15/SHRP	ASDTA	908		20	A SUSSE	266
16/38EF   45017   606   14008ATORIES   16/7126   16/71		16 / SMRF	ASDTA	908		125	A SDDP	107
16/2817		16/SMRP	ASDIT	908		125	ASDIO	620
17,3887		16 / SMRP	ASDIZ	908		167/126	ASDDP	671
22.7MRF 1.3DR 000 LABORATORIES 17, B.F. 198		17 / SMEP	ASDAP	908		195	ASDDA	9
10   10   10   10   10   10   10   10		22/SMEF	TYGSY	900	0 0 1 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	676	ASDAD	900
904/3887 19311 100 22 22 22 22 22 22 22 22 22 22 22 22 2		1410/94		900	LABORALORIES	- C - C - C - C - C - C - C - C - C - C		200
\$\frac{9}{2} \frac{9}{2} \frac			A 30 4 4	7		. ~	E P I P P	512
\$55,888F		504/SMRP	ASDIY	908		22B	WALAA	412
55/38FF A3DAF B06 620 57/38FF A3DAF B06 622 57/38FF A3DAF B06 623 57/38FF B06 622 57/38FF B0		25	A SDB1	=		23	MALAA	549
55/34RF A3DAF 806 622  59/34RF A3DAF 806 622  193/34RF A3DAF 806 622  193/34RF A3DAF 806 622  193/34RF A3DAF 806 622  193/34RF A3DAF 806 622  11,114 A3DAF 664 623  11,114 A3DAF 664 623  14 A3DAF 666 622  22 A3DAF 676 A3DAF 676  16 A3DAF 676 680 622  22 A3DAF 676 A3DAF 676  16 A3DAF 676 680 622  22 A3DAF 676 680 623  14 A3DAF 676 680 623  15/11 A3DAF 676 680  15/12 A3DAF 676 680  15/14 A3DAF 676 680  15/14 A3DAF 676 680  15/14 A3DAF 676 693  15/15 A3DAF 676 693  15/16		55/SMRP	ASDAR	908		450	WALAA	363
91/3HEF ADDAE 8066 622 91/3HEF ADDAE 8066 622 191/3HEF ADDAE 8066 622 191/3HEF ADDAE 8066 224,244-C 191/3HEF ADDAE 8066 224,244-C 11,114 ADDAE 664 226,224-D 11,114 ADDAE 623 26,524-D 11,114 ADDAE 623 66,524-D 11,114 ADDAE 623 66,524-D 125/167 ADDAE 623 623 62,524-D 125/167 ADDAE 626 623 62,524-D 125/167 ADDAE 645 623 7118-D 1118 ADDAE 645 623 7118-D 1718 ADDAE 645 645 645 645 645 645 645 645 645 645		56/SHBP	ASDAF	908		620	HALAA	9 .
91/3887 ASDER 600 600 27,24-C 24,24-C		57 / SMR P	ASDAE	909		622	WALAA	
139.3888		91/3487	ASDA	908		2 1 2 1 2	44140	9 6
11,114 ASDEM 668 25,254-D 11,114 ASDEM 668 65,949 11,114 ASDEM 668 65,954-C 11,114 ASDEM 668 65,954-C 11,114 ASDEM 668 65,954-C 14 ASDEM 656 65,954-C 15 ASDEM 656 65,954-C 125/16 ASDEM 656 65,954-C 125/16 ASDEM 656 65,954-C 125/16 ASDEM 650 65,104-C 126/46 ASDEM 650 65,104-C 12		193/3887	1 2011	900		24 54 4 5 4 5 4 5 4 5 4 5 4 5 4 5 4 5 4	TATEM	0.69
1, 114	PUBC1108AL MAMAGRMENT	2000	ASDPH	99		-	WALFI	96 #
1, 114			ASDPM	546			WALFI	861
11,114 ASDAR 664 59,594-C 114 ASDAR 623 65,654 114 ASDAR 623 65,654 115 ASDR 525 191 115/16 ASDR 660 65,654 116/16 ASDR 660 655 116/16 ASDR 660 651 126/16 ASDR 660 651 136/16 ASDR 650 651 136/16 ASDR 660 651 136/16 ASDR 650 651 136/16 ASDR 660 65		11,114	ASDAC	683		2	WALFI	557
1		11,114	ASDER	199		8 · 5 9 A	WALFI	521
14		<b>=</b> :	ASDAC	678		•	MALFI	7 to 2
6		<b>:</b> :	HADDA.	623		٠		920
15		<u>.</u>	# 70.7 F	00.7		2.5	16143	24.6
125/167		2 '9	ASDIR	535		7 4F	TALE	885
#7	•	25	ASDPA	536		191	WALFI	503
125/167 ASDRM 616 680 254 455 6716 ASDRM 680 680 255 855 855 855 855 855 855 855 855 855		-	ASDIR	268		192	WALFI	533
6/16 ASDEM 680 14/11 ASDEM 683 16 ASDEM 693 20,20A/16 ASDEM 693 22,16 ASDEM 680 125/11 ASDEM 829 156/46 ASDEM 837 14 ASDEM 837 16 ASDEM 645 17 71 ASDEM 645 16 ASDEM 645 17 71 ASDEM 645 18,18A-E,G,H 71 ASDEM 645 16 ASDEM 645 17 71 ASDEM 645 18,18A-E,G,H 71 ASDEM 645 18,18A-E,		125/167	ASDPH	919		254	WALFI	295
16 ASDEM 693 20,204/16 ASDEM 693 22/16 ASDEM 693 22/16 ASDEM 690 125/11 ASDEM 771 126/46 ASDEM 706 126/46 ASDEM 837 14 ASDEM 837 16 ASDEM 606 18,184-E,G,H 16 ASDEM 606 18,184-E,G,H 16 ASDEM 645 171 18 ASDAM 645 18 ASDAM 645 18 ASDAM 645 19 ASDAM 645 10 ASDAM 645 11 ASDAM 645 11 ASDAM 645 11 ASDAM 645 12 ASDAM 645 13 ASDAM 645 14 ASDAM 645 15 ASDAM 645 16 ASDAM 645 17 ASDAM 645 18		91/9	A SORE	089		255	INTE	559
22,16 ASDEN 538 20,20A 71A ASDEN 680 20,20A 71A ASDEN 680 771 450 450 126/46 ASDEN 706 802 651 651 651 156/485 ASDEN 802 653 653 653 653 653 653 653 653 653 653			12021	n 0		. 4 . 4	14141	4 00
22/16		20.204/16	ASDEA	2 60		20.204	WALMI	529
46 ASSEM 771 ASSEM 750 ASSEM 771 ASSEM 706 ASSEM 706 ASSEM 706 ASSEM 706 ASSEM 829 ASSEM 829 ASSEM 829 ASSEM 829 ASSEM 837 ASSEM 845 ASS		22/16	ASDEN	089		7.7	WALML	423
125/11 ASDRM 706 651 126/46 ASDRM 802 156/465 ASDRM 829 156/465 ASDRM 827 14 ASDRM 837 16 ASDRM 606 16 ASDRM 606 16 ASDRM 645 17 71A 18 ASDA 71A 18 ASDA 629 18 18 18 18 18 18 18 18 18 18 18 18 18 1		94	ASDRI	171		150	WALMI	427
156/46 ASSER 602 653 156/465 ASSER 602 465 ASSER 629 465 ASSER 837 14 ASSAV 580 16 ASSAV 606 59,50A-C 16 ASSAL 645 39/16 ASSAL 623 1718 718 718 719 719 719 719 719 719 719 719 719 719		125/11	T SDE	406		651	WALML	80 G
405 ASSEM 0.29 405 ASSEM 0.29 14 ASSEM 560 16 ASSEM 606 16 ASSEM 606 39/16 ASSEM 623 450 450 450		126/46		202		229	1 - 4 - 2	0 0
14 ASDAY 580 20,20A 16 ASDAY 606 59,59A-C 16 ASDAY 615 71 71 71 80 80 80 80 80 80 80 80 80 80 80 80 80		150/405	# 20 F	66.9		8	=	
16 ASDAN 606 51 51 59,59A-C 16 ASDAL 615 71A 71A 56/16 ASDAX 623 450 450 450 450	一日の日本の日本の日本の日本の日本の日本の日本の日本の日本の日本の日本の日本の日本		P 400 4	0 60				683
ASDAR 645 59,59A-C ASDAR 623 718 718 718 718 719 719 719 719 719 719 719 719 719 719		9	ASDAM	909		21	WALPO	989
ASDAX 623 71 ASDAX 623 71A 71B 71D		92	ANGSA	949		1594	WALPO	524
ASDAX 623 71A 71B 71B 71B 71D		39/16	ASDAL	615		7.1	WALPO	991
		56/16	ASDAX	623		7 1 A	WALPO	542
						8 .	WALPO	636
						710		20.4
						707		0 1 4 1 4
ABURA						00	MALPO	818
50						2 47	AFWAL	96#
						ŝ	AFWAL	532

RAZAGOSOSTIENASSOSSASSAS INSTITUTOS SAIRINOSOS AS ARBITAGOS AS ARBITAGOS AS ARBITAGOS AS ARBITAGOS AS ARBITAGOS A

CESCENSES PERFORMED POLICIOLES SESSIONS (CONTRACTO

#### APPENDIX C

# GLOSSARY OF TERMS

AA Avionics Laboratory

AFIT Air Force Institute of Technology

AFLC Air Force Logistics Command

AFSC Air Force Systems Command

AFWAL Air Force Wright Aeronautical Laboratories (also WAL)

AMD Aerospace Medical Division

ASD Aeronautical Systems Division

EN Deputy for Engineering

FI Flight Dynamics

LOG Logistics (Command)

MAC Military Airlift Command

MCP Military Construction Project

ML Materials Laboratory

R&D Research and Development

SAC Strategic Air Command

SMEF Systems Management Engineering Facility

SPO Systems Program Office

TAC Tactical Air dommand

WAL Wright Aeronautical Laboratories

ENDOUGH STREET STREET, STREET, WOODE, WOODE,

SECURITY CLASSIFICATION OF THIS PAGE (When Date Entered)

REPORT DOCUMENTATION PAGE		READ INSTRUCTIONS BEFORE COMPLETING FORM
1. REPORT NUMBER	2. GOVT ACCESSION NO.	3. RECIPIENT'S CATALOG NUMBER
	HDA1 1991	5
4. TITLE (and Subtitle)		5. TYPE OF REPORT & PERIOD COVERED
INTEGRATED FACILITIES MANAGEMENT PLAN		Final Report
		6. PERFORMING ORG. REPORT NUMBER
7. AUTHOR(e)		AS301  B. CONTRACT OR GRANT NUMBER(*)
Douglas K. Ault		or converge on season sometimes
John H. Cable		
William A. Woodring		F33657-83-C-0444
9. PERFORMING ORGANIZATION NAME AND ADDRESS Logistics Management Institute		10. PROGRAM ELEMENT, PROJECT, TASK AREA & WORK UNIT NUMBERS
4701 Sangamore Road, P.O. Box 9489		
Washington, D.C. 20016		
11. CONTROLLING OFFICE NAME AND ADDRESS		12. REPORT DATE
THE CONTROLLING OFFICE NAME AND ADDRESS		30 April 1984
Aeronautical Systems Division		13. NUMBER OF PAGES
Wright-Patterson AFB, Ohio		
14. MONITORING AGENCY NAME & ADDRESS(If different from Controlling Office)		18. SECURITY CLASS. (of this report)
		UNCLASSIFIED
		154. DECLASSIFICATION/DOWNGRADING SCHEDULE
16. DISTRIBUTION STATEMENT (at this Report)		
"A" Approved for public release; distribution unlimited.		
17. DISTRIBUTION STATEMENT (of the electract entered in Block 20, If different from Report)		
18. SUPPLEMENTARY NOTES		
19. KEY WORDS (Continue on reverse side if necessary and identify by block number)		
Facilities Planning, Facilities Management, Military Construction Program, Master Plan, Base Comprehensive Plan		
20 ASSESSED CONTRACTOR OF THE PROPERTY OF THE		
20. ABSTRACT (Continue on reverse olds if responsely and identity by block number)		
Report investigates current facility deficiencies and analyzes requirements		
for the Aeronautical Systems Division at Area B, Wright-Patterson Air Force Base, Ohio. An integrated Facilities Management Plan is presented which in-		
cludes construction, relocation and demolition requirements. Organizational		
management actions to support implementation of the plan are also discussed.		
Appendices to the report present information on decision-support methodologies		
used in evaluating various facilities alternatives.		

DO 1 JAN 73 1473 EDITION OF 7 NOV 65 IS OBSOLETE
